



IMJIN PARKWAY WIDENING & ROUNDABOUT PROJECT

Construction Activities Update: December 15 – December 26, 2025

PLEASE BE ALERT!

The enforceable speed limit through the construction zone is 25 MPH

PLEASE REMEMBER TO CHECK THE PROJECT WEBSITE FOR THE MOST CURRENT ROADWAY CLOSURE INFORMATION AT www.imjinparkway.com

TIPS FOR DRIVING ROUNDABOUTS:

- **VEHICLES ALREADY IN THE ROUNDABOUT HAVE THE RIGHT OF WAY**
- **VEHICLES MERGING INTO THE ROUNDABOUT:**
 - **CHECK FOR PEDESTRIANS CROSSING IN THE AREA**
 - **YIELD TO VEHICLES IN THE ROUNDABOUT AND MERGE SAFELY**

What's Happening in the Next 2 Weeks (December 15 – December 26)

Day Shift

- Complete planting native plants.
- Continue working on list items to achieve project completion.
- Complete installing permanent striping and markings.
- Begin/complete markings on multi-use trail.

Closures: No closures are anticipated. However, be alert for traffic lane shifts while we complete pavement markings. There may also be some limited flagging on side streets while striping/markings are completed.

Please check the website for the latest information on closures www.imjinparkway.com

Activities That Took Place Last Week (December 8 – 12)

- Continued planting landscape materials (native plants and trees).
- Complete approximately 95% of all striping and markings; remainder to be completed next week.

Future Construction Activity and Information: What's Planned in the Future?

- **Phase 4: Final permanent pavement striping and markings!** We will complete all pavement stripings and markings this week (week of 12/15). The roadway is currently open to it full and final configuration! We still have striping and markings to be installed on the multi-use path/trail to be scheduled but this will not impact the roadways. **THANK YOU FOR YOUR PATIENCE!**
- **Artwork installation at roundabouts.** We are working with the contractor and his vendor to finalize the final details of the artwork. Delivery/installation is anticipated in March of 2026.




IMJIN PARKWAY WIDENING & ROUNDABOUT PROJECT

PROGRESS PHOTOS



Thermoplastic striping material is heated to over 400 degrees in boilers mounted on the truck. The heated material is then extruded through a nozzle onto the pavement. A nozzle mounted just behind the extruder nozzle "blows" glass beads onto the stripe to enhance reflectivity at night.

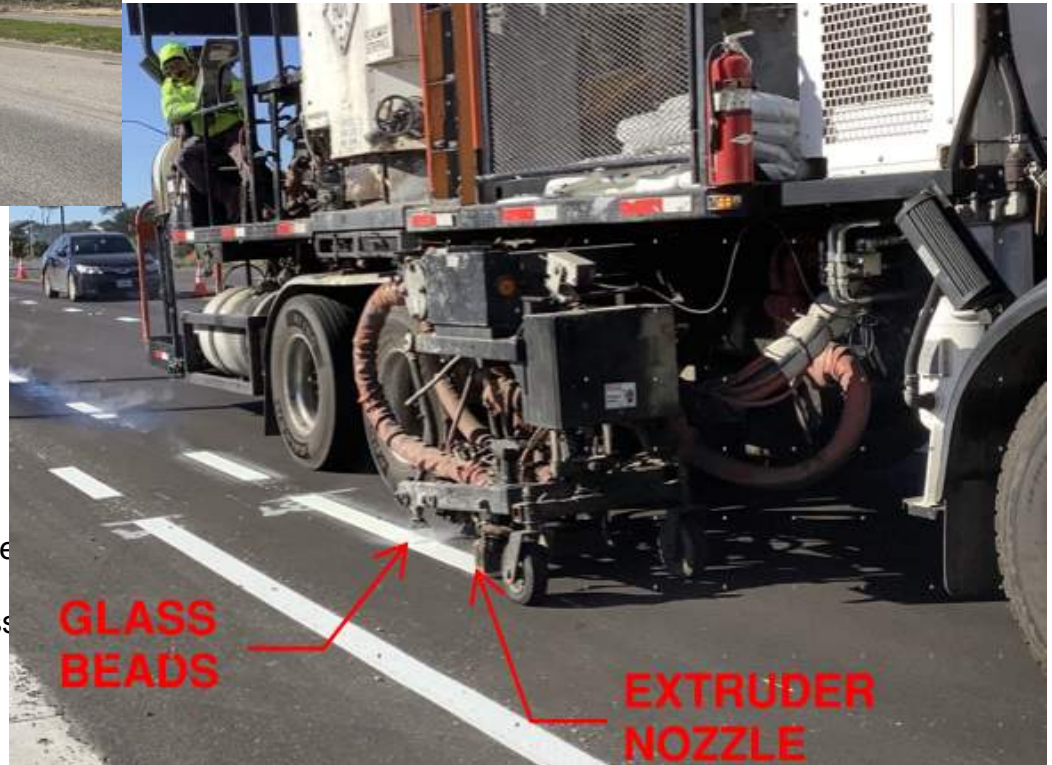

Smaller motorized or "walk-behind" equipment is used to install the heated thermoplastic material for the various markings like arrows and cross walks



IMJIN PARKWAY WIDENING & ROUNDABOUT PROJECT



Imjin Parkway at Reservation Road

Imjin Parkway at Abrams Drive



Imjin Parkway at Imjin Road

How to Stay Informed

- Please visit the project website at www.imjinparkway.com or contact Edrie De Los Santos (City of Marina) at 831.884.1212
